

— Welcome —

A few reminders

- Please sign in.
- Silence phones and electronic devices.
- Feel free to ask questions throughout the presentation; please state your name, agency and whether you represent the business or technical area.
- We want to hear what you have to say; one speaker at a time.
- For those on the phone, set your phone to mute.
- Share CISS information with your agency counterparts.
- Please follow up with a CJIS team member with your comments, suggestions and feedback.
- Thank you for attending.



State of Connecticut
Criminal Justice Information System

Connecticut Information Sharing System Status Meeting
October 9, 2013

Agenda

- ▶ CISS Status
 - ▶ CJIS Immediate Action Items
 - ▶ Wave 0, Version 1.5 Update
 - ▶ RMS Network & Certification Update
 - ▶ Search Release 1 Update
 - ▶ Wave 1 – UAR Workflow Update
- ▶ Questions and Answers


CJIS Program Update

Immediate Action Items

- Stakeholder management
 - Interaction, decision making, impact on resources
- CJIS Security Policy
- Project plan, release strategy, organization

CISS Implementation Dates

Wave 0, Version 1.5 (Technical Architecture)

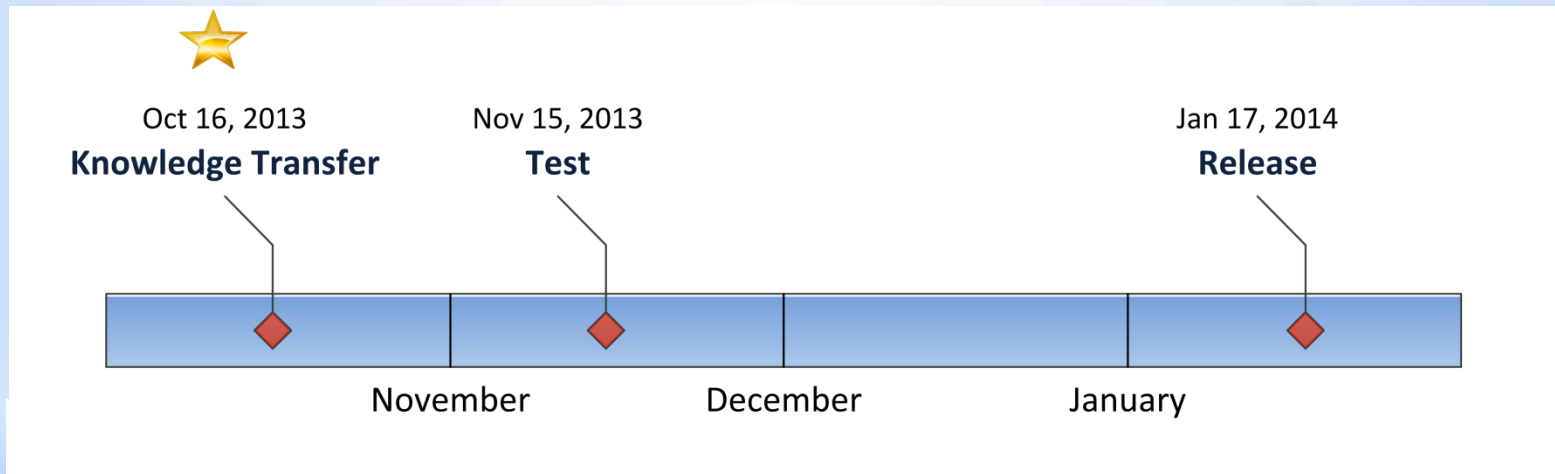

Wave 0, Version 1.5 Update

➤ **Current Status**

- Completed build-out (cloning) of Production environment
- Completed installation of FileNet ECM System
- Began release management for CISS environments
 - Documenting the Patch and Backup Management Plan
- Approval of vendor Architecture Design build-outs underway

➤ **Next Steps**

- Document the Recovery Management Plan
- Perform environment cut-over processes
 - Review release controls and post-cloning cleanup
- Perform High Availability testing

RMS Network Update

- Begin installation of CJIS network routers
- Begin configuration and deployment of police department routers with pilot municipalities:
 - Newington
 - Wethersfield
 - Glastonbury
- Kicked off coordination of equipment upgrades and purchases with towns
 - 50% of towns have purchased equipment

RMS Certification Program Update

➤ **Current Status**


- Completed the Draft RMS Certification requirements and preparing for stakeholder and pilot vendors' review

➤ **Next Steps**

- Perform an RMS Certification confirmation process – Target Date Late October
- Assemble draft RMS Certification program materials – Target Mid-November
- Disseminate draft requirements to CJIS Community and Vendors to solicit feedback – Target Late November
- Begin pilot testing with 3 vendors to implement the Information Exchanges for W1 – Target Early January

CISS Implementation Dates

Search Release 1 (PRAWN, OBIS)

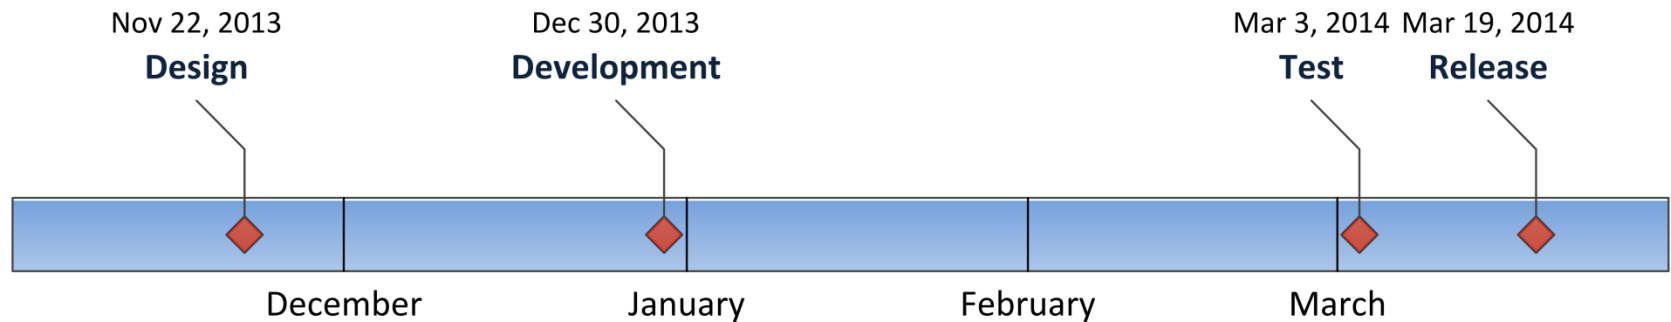

Search Release 1 (SR1) Update

➤ **Current Status**


- Replicating PRAWN and OBIS systems
- Updating User Interface requirements and design documents
- Confirming testing strategy and test cases
- Developing software for search sources, search functionality, and System Administration

➤ **Next Steps**

- Hold LEA review of User Interface prototype – Late October
- Develop computer based & instructor led training curriculum – Starts October 21
- Develop deployment strategy – Starts late October

CISS Implementation Dates

Wave 1 (UAR)

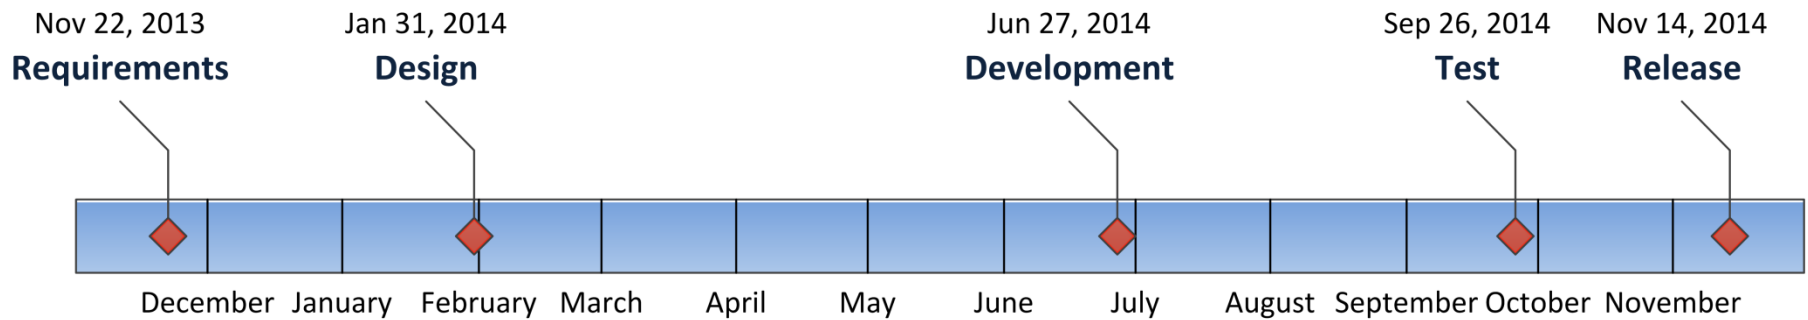

Wave 1 – UAR Workflow Update

➤ Current Status

- Wave 1 (W1) scope expanded to include:
 - Ability for users to submit scanned arrest paperwork to CISS for situations where their RMS system is unable to do so
 - CONNX replication of RMS systems to facilitate bulk upload of historical data as well as the ability to transmit new or updated UARs to CISS on an ongoing basis
- Met with stakeholders to confirm detailed requirements
- 30% of W1 requirements completed and submitted to Xerox

Wave 1 – UAR Workflow Update (cont'd)

➤ Next Steps

- Continue to work with stakeholders on requirements:
 - GFIPM security mapping for W1
 - Several working sessions scheduled in mid-October
 - Involves all agencies
 - Information exchanges going to CSSD
 - Including how CSSD will consume CISS data
 - Architecture overview meeting scheduled on October 16
 - Several detailed working sessions to be held after October 16
 - Redactions and restrictions for UARs
 - Working with Judicial to determine how CRMVS can be used to notify CISS of erasures
 - CJIS Community Portals for W1
 - Working session with DOC & BOPP conducted on October 8
 - Working sessions to be scheduled with DCJ, Court Operations, DPDS
 - User initiated alerts
 - Working session to be scheduled with all agencies in October
- Complete all W1 requirements by November 22, 2013

Comments

We appreciate your feedback.

Please send us your comments, questions & suggestions.

Sean Thakkar — Sean.Thakkar@ct.gov

Rick Hegwood — Richard.Hegwood@ct.gov

Rick Ladendecker — Rick.Ladendecker@ct.gov

Nance McCauley — Nance.McCauley@ct.gov

Next meeting: November 13, 2013

QUESTIONS?

Appendix 1: Acronyms

CJIS Web Site -- Acronyms list online

AFIS = Automated Fingerprint Identification System
AST = Application Support System
BEST = Bureau of Enterprise Systems and Technology
BICE = Bureau of Immigration and Customs Enforcement
BOPP= Board of Pardons and Paroles
CAD = Computer Aided Dispatch
CCH= Computerized Criminal History (DESPP)
CIB = Centralized Infraction Bureau (Judicial)
CIDRIS = Conn. Impaired Driver Records Information System
CISS = Conn. Information Sharing System (CJIS)
CIVLS = CT Integrated Vehicle & Licensing System
CJIS = Criminal Justice Information System
CJPPD = Criminal Justice Policy Development and Planning Division
CMIS = Case Management Information System (CSSD)
COLLECT = CT On-Line Law Enforcement Comm. Teleprocessing Network
CPCA = Conn. Police Chiefs Association
CRMVS = Criminal and Motor Vehicle System (Judicial)
CSSD = Court Support Services Division (Judicial)
DCJ = Division of Criminal Justice
DAS = Dept. of Administrative Services
DESPP = Dept. of Emergency Services & Public Protection
DEMHS = Dept. of Emergency Management & Homeland Security

DMV = Dept. of Motor Vehicles
DOC = Department of Correction
DOIT = Dept. of Information Technology
DPDS = Div. of Public Defender Services
GIS = Geographic Information System
IST = Infrastructure Support Team
JMI = Jail Management System
JUD = Judicial Branch
LEA = Law Enforcement Agency
LAW = Local Law Enforcement (e.g., DPS, CPCA)
LIMS = State Crime Laboratory Database
MNI = Master Name Index (DESPP)
OBIS = Offender Based Information System (Corrections)
OBTS = Offender Based Tracking System
OCPD = Office of Chief Public Defender
ORI = Originating Agency Identifier
OSET = Office of Statewide Emergency Telecommunications
OVA = Office of the Victim Advocate
OVS = Office of Victim Services
PERU = Passenger Endorsement Review Unit
POR = Protection Order Registry (Judicial)
PRAWN = Paperless Re-Arrest Warrant Network (Judicial)
PSDN = Public Safety Data Network
RMS = Records Management System
SCO= Superior Court Operations Div. (Judicial)
SOR = Sex Offender Registry (DESPP)
SPBI = State Police Bureau of Identification (DESPP)
SLWRS = Special Licensing and Weapons Registration System (DESPP)
SLFU= Special Licensing of Firearms Unit (DESPP)

UAR = Uniform Arrest Report

Technology Related

ADFS = Active Directory Federated Services
COTS = Computer Off The Shelf (e.g., software)
ETL = Extraction, Transformation, and Load
FEA = Federal Enterprise Architecture
FIM = Forefront Identity Manager (Microsoft)
FIPS = Federated Information Processing Standard
GFIPM = Global Federated Identity & Privilege Management
GUI = Graphical User Interface
IAFIS = Interactive Automated Fingerprint Information System*
IEPD = Information Exchange Package Document
III = Interstate Identification Index
LAN = Local Area Network
LEXS = Logical Entity eXchange Specifications
N-DEx = Law Enforcement National Data Exchange
NIEM = National Information Exchange Model
PCDN = Private Content Delivery Network
POC = Proof of Concept
RDB = Relational Database
SAN = Storage Area Network
SDLC = Software Development Life Cycle
SOA = Service Oriented Architecture
SQL = Structured Query Language

Rev 6.3.2013
